BRUHAT BANGALORE MAHANAGARA PALIKE

Name of Work: Improvements, Restoration to roads and drains at Dasarahalli, Saraipalya and Rachenahalli Surrounding Areas in ward no. 06

Sl No	Description of Work	Unit	Tender Qty	Executed Qty	% of Work Completed
1	Removing and refixing stone slabs of drains and pointing in CM (1:3) (P.No-27,I No-5.33,KPWD SR 2018-19)	Sqm	3157.11	1994.00	63.16
2	KSRRB 300-1 Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications(I No-19.1, P No-143), 10km lead	Cum	8670.96	4946.08	57.04
3	Providing granite slabs of selected quality roughly dressed and fixed in cement mortar (1:6) including fixing curing etc., complete. (P.No-27,I No-5.31.1, KPWD SR 2018-19), 7.5cms thick	Sqm	2104.74	1134.38	53.90
4	KSRB 4-1.2 : Providing and laying in position plain cement concrete of Mix 1:3:6 with OPC @ 220kgs, with 40mm and down size graded granite metal coarse aggregates @0.892cum and fine aggregates @ 0.465cum machine mixed, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation including cost of all materials, labour, HOM curing complete as per specifications. (P.No-13,I No-4.2,KPWD SR 2018-19)	Cum	570.06	569.49	99.90
5	Providing and laying plain/reinforced cement concrete for side drains using M20 nominal mix concrete with OPC at 300 kgs. with 20mm and down size granite metal coarse aggregates at 0.69 cum and fine aggregates at 0.43 cum machine mixed, well compacted for walls and bottom including centering, shuttering, cost of materials, HOM of machinery, curing etc., complete excluding cost of steel as per MORTH specification No. 1500, 1700, 2200. including cost of materials, labour, HOM complete as per specificationsdo- Wall & bottom thickness 15cm (I No-37.59.2,P No-271,KPWD SR 2018-19)	Cum	1188.35	1187.59	99.94
6	KSRRB M2200-6. Providing T.M.T. steel reinforcement for R.C.C. work including straightening, cutting, bending, hooking, placing in position, lapping and/or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per disign (laps, hooks and wastage shall not be measured and paid) cost of materials, labour, HOM complete as per specification.(I No-28.8.2,P No-229)	Tn	76.47	76.42	99.93
7	Providing and Fixing pre cast covering Slab 100mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of alll materials, labour,hire charges of machinery, loading, unloading, lead and lift,transportation etc ,complete.As per Engineer incharge. (Data Rate)	Sqm	2751.00	2749.23	99.94
8	Providing and Fixing pre cast covering Slab 250mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of alll materials, labour,hire charges of machinery, loading, unloading, lead and lift,transportation etc ,complete.As per Engineer incharge. (Data Rate)	Sqm	400.80	400.11	99.83
9	KSRRB M300-14. Excavation for roadwork in all types of soil by mechanical means including cutting and loading to tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transportation with a lead of 1.00 km and complete as per specifications MORTH Specificatio MORTH Specification No.301Loading and unloading with 10km lead= (I No-19.14,P No-143,KPWD SR 2018-19), 10kms lead	Cum	10974.66	7281.35	66.35

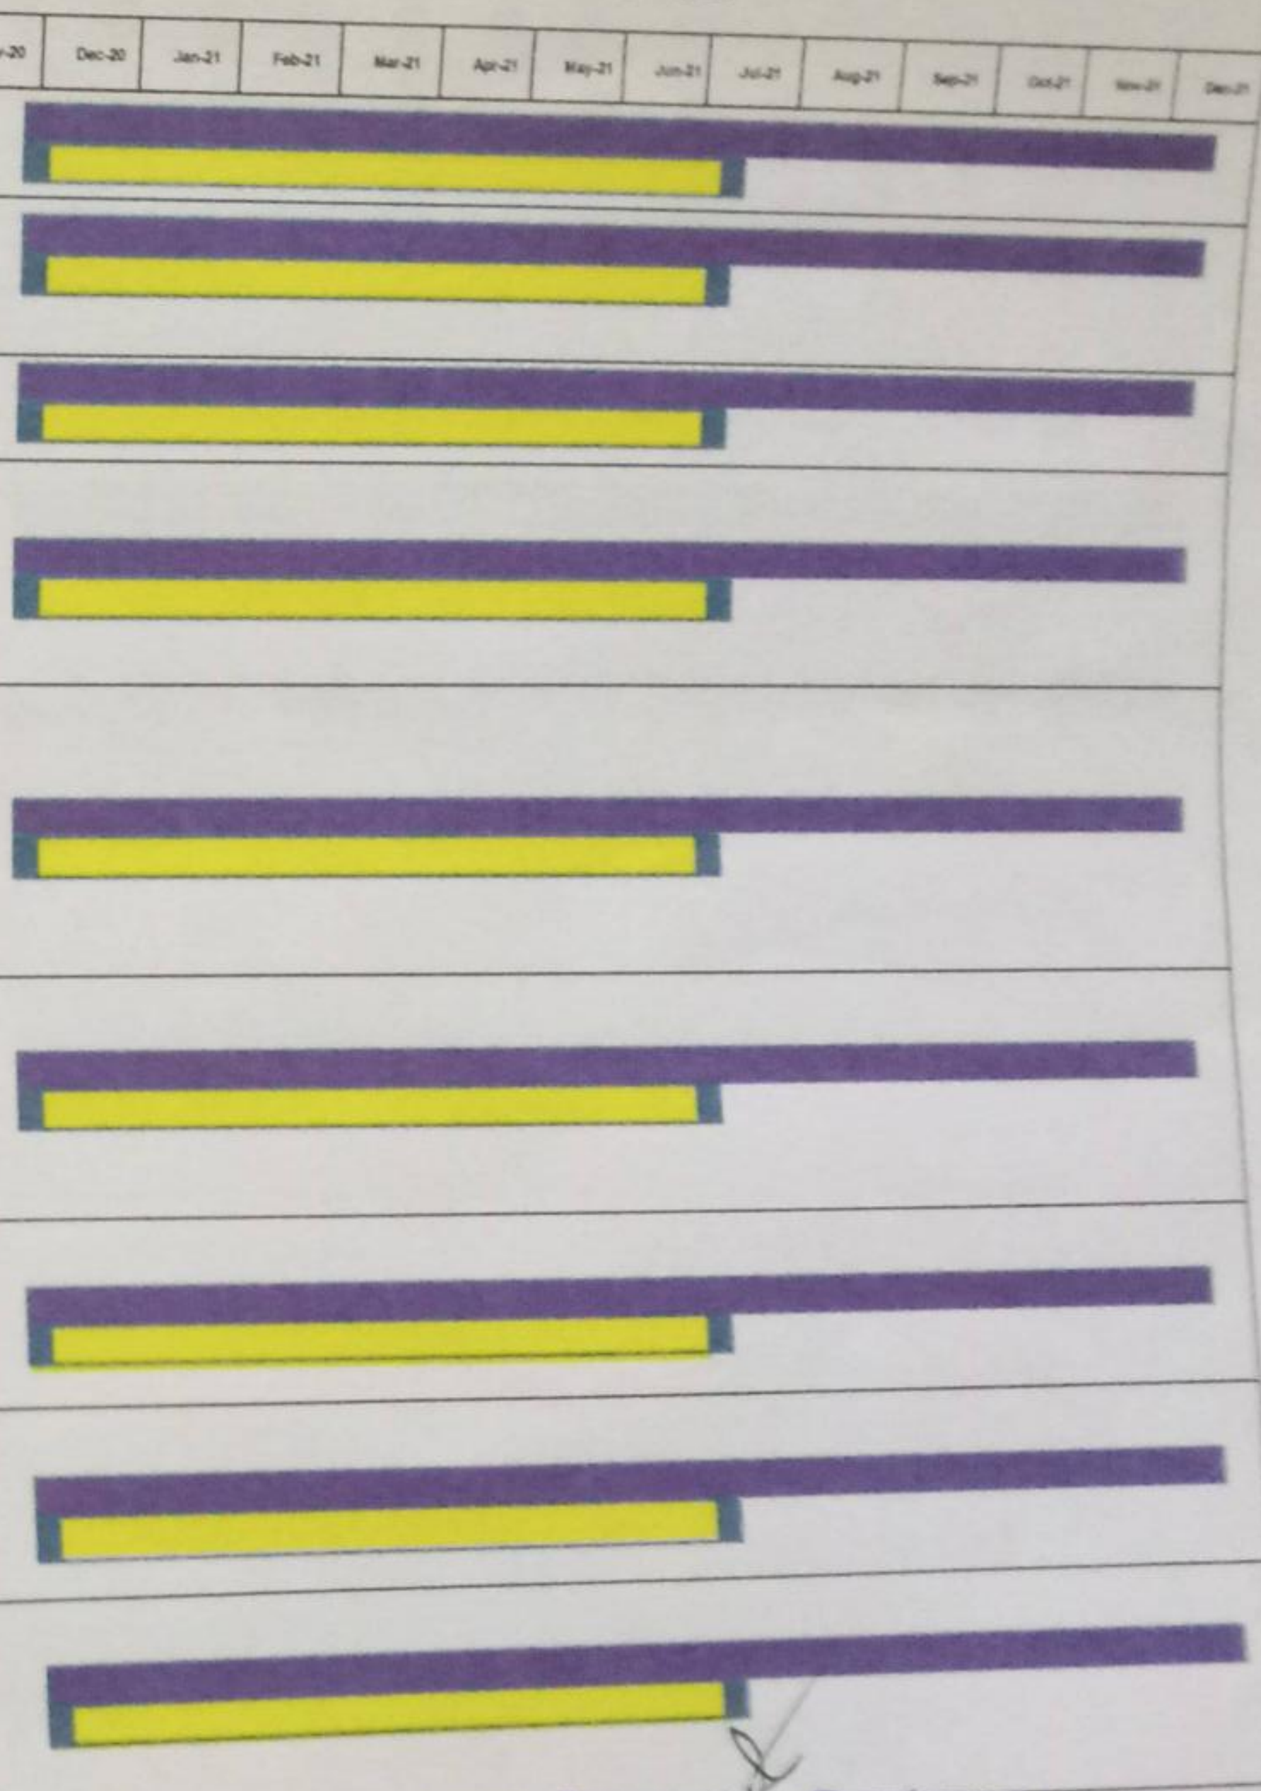

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Scanned by TapScanner

10	KSRRB 300-46. Scarifying by mechanical means stone metal crust 50mm to 100mm thick by along with 20mm premix carpet / surface dressing and stacking of old serviceable materials including cost of all labour charges, HOM complete as per specifications.(P.No-146,I No-19.52)	Sqm	49195.20	29372.80	59.71	
11	Providing, laying, spreading and compacting Stone dust / Grit 4.75 mm to 0.075 mm specifications including pre mixing the material with water at OMC in mechanical mix plant carriage of mixed materials by tipper to site, laying in uniform layers. (P.No-II,Sl No-45)	Cum	6026.94	3505.83	58.17	
12	KSRRB M400-17. Providing, laying, spreading and compacting cushed stone aggregates of granite / trap / basalt to wet mix macadam specifications including pre mixing the material with water at OMC in mechanical mix plant carriage of mixed materials by tipper to site, laying in uniform layers with paver in sub-base/base course on well prepared surface and compacting with vibratory roller to achieve the desired density complete as per specifications(P.No-155,I No-20.18)	Cum	19751.74	9853.00	49.88	
13	KSRRB M500-6. Providing and applying primer coat with S.S. bitumen emulsion on prepared surface of granular base such as WMM including cleaning of road surface and spraying primer at the rate of 0.60 kg / sqm using mechanical means complete as per specifications Clause 502 of MORTH V revision(P.No-158,I No-21.6), issue rate dated 03-01-2020	Cum	85777.40	18917.20	22.05	
17	Providing and laying bituminous concrete 40mm thick with hot mix plant, using crushed aggregates of specified grading, premixed with bituminous binder and filler, transporting the hot mix to work site, laying with a paver finisher to the required grade, level and alignment, rolling with smooth wheeled, vibratory and tandem rollers to achieve the desired compaction in all respects complete as per specifications. Clause 507 of MORTH V revision as per IRC SP-53-2015. using 40-60 TPH capacity HMP with mechanical paver grading II (30-45mm) with 5.4 % of modified bituminus binder consisting of 4.97% of VG-30 bitumen (60/70 grade) and 0.43% of plastomeric thermoplastics (waste plastic)(P.No-171,I No-21.78.12), issue rate dated 03-01-2020	Cum	4150.58	756.69	18.23	
19	KSRRB M200-24. Dismantling of cement concrete pavement by mechanical means using pneumatic tools, breaking to pieces not exceeding 0.02 cum in volume and stock piling at designated locations and disposal of dismantled materials upto a lead of 1000 metrers, stacking serviceable and unserviceable materials seperately complete as per specifications. MORTH Specification No. 202.(I No-18.47,P No-140)	Cum	1076.70	829.98	77.09	

= Planned %
= Executed %

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

PREETHI CAD CONSULTING
ENGINEERS PVT. LTD.
48/43, 6th Main Road, Jnanajyothi Nagar,
Jnana Bharathi, Bangalore - 560 056.

Scanned by TapScanner
